McCraken Drive Reconstruction
Tender Program Rev 1 - Post Tender

neo infrastructure [sa] civil engineering contractors

ID	Task Name	Duration	Start	Finish
1	Award	1 day	Wed 20-02-19	Wed 20-02-19
4	Preliminaries (Project Management Plans, Permits etc)	3 days	Thu 21-02-19	Mon 25-02-19
5	Procurement	5 days	Thu 21-02-19	Wed 27-02-19
6	Resident / Business notifications	1 day	Thu 21-02-19	Thu 21-02-19
2	Survey Set out	1 day	Mon 25-02-19	Mon 25-02-19
3	Service Locations	1 day	Mon 25-02-19	Mon 25-02-19
7	Mobilisation	1 day	Mon 25-02-19	Mon 25-02-19
8	**Site Works**	**33 days**	**Tue 26-02-19**	**Fri 12-04-19**
9	Install Traffic Traffic Control	1 day	Tue 26-02-19	Tue 26-02-19
10	Remove existing kerb and driveways	3 days	Tue 26-02-19	Thu 28-02-19
11	Make driveways accessible	3 days	Tue 26-02-19	Thu 28-02-19
12	Stormwater Pipe and pit Installation	4 days	Tue 26-02-19	Fri 01-03-19
15	Remove fencing and signage	1 day	Thu 28-02-19	Thu 28-02-19
16	Asphalt saw cutting	1 day	Thu 28-02-19	Thu 28-02-19
24	Lighting caisson and trenching	1 day	Mon 04-03-19	Mon 04-03-19
13	Box out for parking bays, kerbing, driveways and footpath	8 days	Tue 05-03-19	Fri 15-03-19
14	Trim and Compact Subgrade	1 day	Mon 18-03-19	Mon 18-03-19
17	Subbase to parking bays and kerbing	3 days	Tue 19-03-19	Thu 21-03-19
18	Kerbing	4 days	Fri 22-03-19	Wed 27-03-19
23	Footpath and driveway subbase	2 days	Tue 26-03-19	Wed 27-03-19
19	Back up kerb	2 days	Wed 27-03-19	Thu 28-03-19
20	Basecourse construction parking bays	2 days	Thu 28-03-19	Fri 29-03-19
22	Base to front of kerb	1 day	Mon 01-04-19	Mon 01-04-19
21	Footpath and driveway construction	5 days	Tue 02-04-19	Mon 08-04-19
26	Electical Works	3 days	Tue 09-04-19	Thu 11-04-19
25	Asphalt sealing works	1 day	Fri 12-04-19	Fri 12-04-19
27	Practical Completion	1 day	Fri 12-04-19	Fri 12-04-19

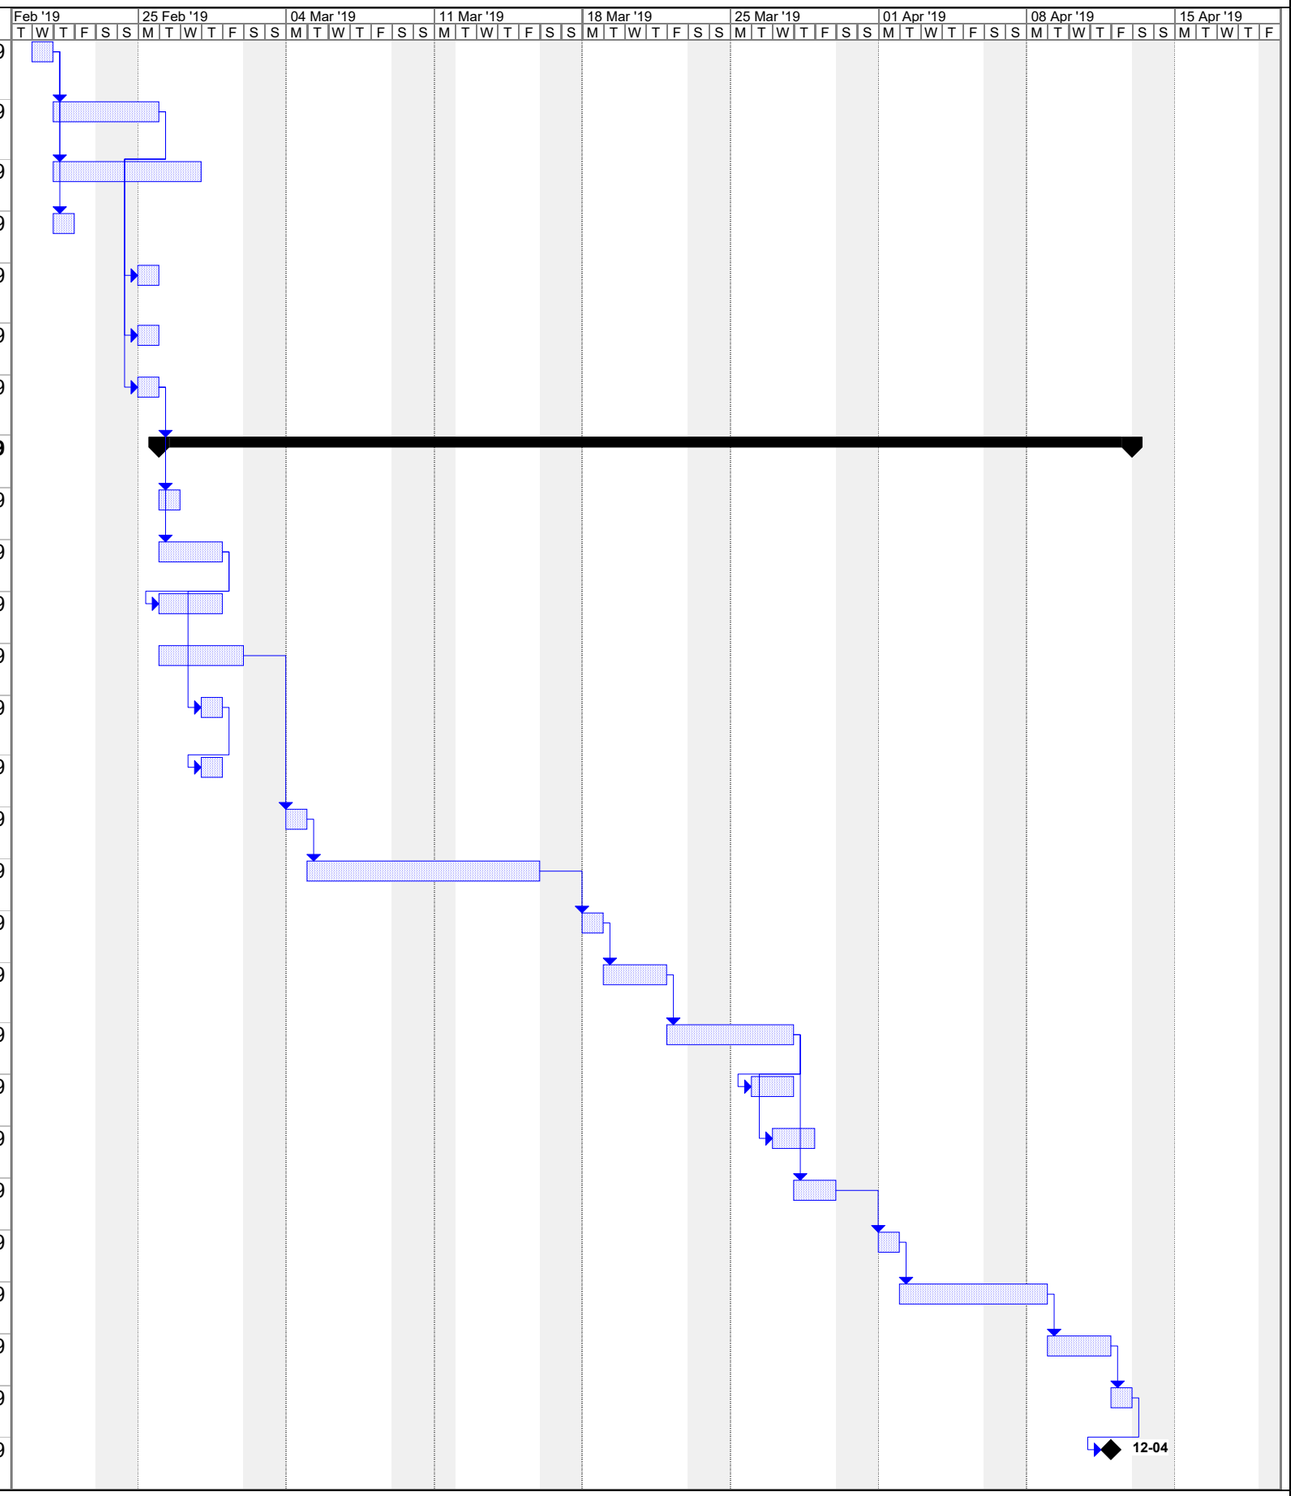

McCracken Road Program Rev B (Post Tender

Task | Progress | Summary | External Tasks | Deadline
Split | Milestone | Project Summary | External Milestone
